ATELIER DENSIDADES
GABINETE DE ARQUITECTURA,
ENGENHARIA E TÉCNICAS AFINS,
IMAGENS 3D, DESIGN E DESIGN DE MOBILIÁRIO

CENTRO EMPRESARIAL
E INDUSTRIAL DE LOULÉ
CAMPINA DE BAIXO, LOTE 1 - SALA 4
8100-285 LOULÉ

t 00351 289 432 670
f 00351 289 432 671

info@densidades.pt
www.densidades.pt

Loulé, 30 May 2015

SITE VISITATION REPORT – May.2015

SITE VISITATION AND CLARIFICATION OF WORKS ACCORDING TO DETAIL PROJECT

Site photos

Handled Issues:

1 Verification and clarification of concrete beams in garage area at floor level for casting of basement concrete slab

- Solved, corrected by structural engineer and revised drawings updated on site

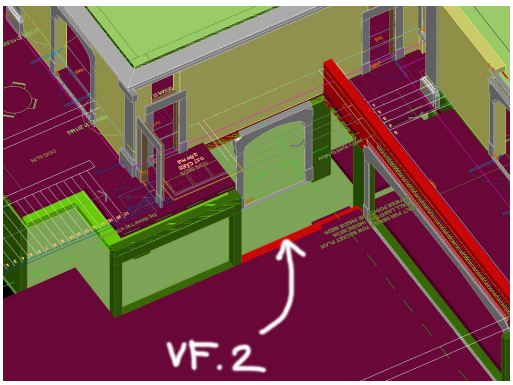

2 Verification and clarification of concrete beam above basement window near pool table area (no image)

- Solved, corrected by structural engineer and revised drawings updated on site

(continues)

ATELIER DENSIDADES É UMA MARCA REGISTADA DA MUTABILIS9 ARTE E ARQUITECTURA,LDA.

DENSIDADES
ATELIER

ATELIER DENSIDADES
GABINETE DE ARQUITECTURA,
ENGENHARIA E TÉCNICAS AFINS,
IMAGENS 3D, DESIGN E DESIGN DE MOBILIÁRIO

CENTRO EMPRESARIAL
E INDUSTRIAL DE LOULÉ
CAMPINA DE BAIXO, LOTE 1 - SALA 4
8100-285 LOULÉ

t 00351 289 432 670
f 00351 289 432 671

info@densidades.pt
www.densidades.pt

Loulé, 30 May 2015

3 Verification and clarification of concrete beams in garage area at ceiling level for casting of ground floor concrete slab
- Solved, corrected by structural engineer and revised drawings updated on site

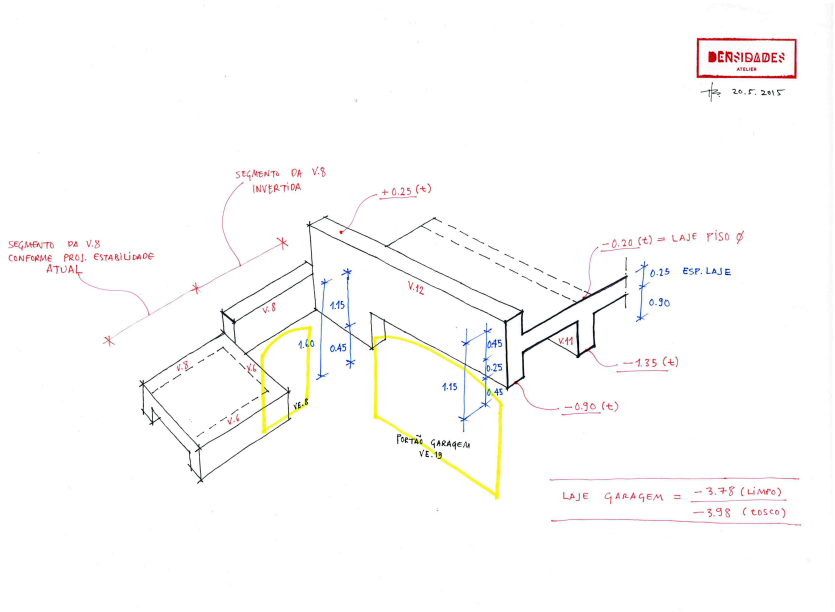

4 Sewage piping verified since one sewage box had no sloping angle from previous. Change in layout proposed by Lux and agreed by email exchange between myself, Lux and Andrew.
- Solved, no costs involved, should actually be a discount made to James regarding point 20.2 of Lux's quote since, to my knowledge the sewage pumps will not be installed.

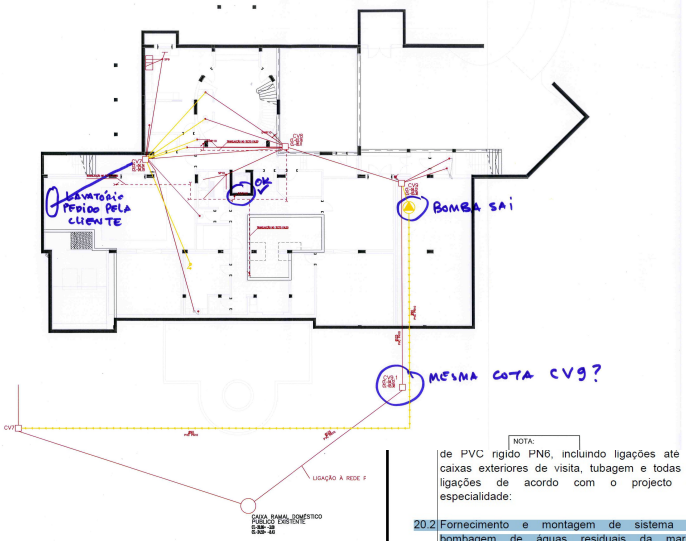

	NOTA:				
	de PVC rígido PN6, incluindo ligações até as caixas exteriores de visita, tubagem e todas as ligações de acordo com o projecto da especialidade:	vg	1,00	4.485,00 €	4.485,00 €
20.2	Fornecimento e montagem de sistema de bombagem de águas residuais da marca ***"Grundfos"*** composto por:				
	- Bombas de águas residuais da marca ***"Grundfos"*** modelo ***"Unilift AP 50B.50.08.3"***.	un	2,00	776,25 €	1.552,50 €
	- Quadro AVL QE ALT+AL 3N RA23A+RVSFT DF 1,8 - 2,8.	un	1,00	473,34 €	473,34 €
	- Interruptor de nível Idro 10mts.	un	2,00	28,52 €	57,04 €
	- Contra peso para interruptor de nível.	un	2,00	3,22 €	6,44 €
	- Interruptor de nível SLC 10E com 10mts.	un	2,00	88,55 €	177,10 €
	- Tubagem e montagem para electrobombas de águas residuais.	un	1,00	862,50 €	862,50 €
20.3	Escavação em terra compacta ou saibro, na abertura de caboucos e valas para colocação de tubagens das redes exteriores de esgotos domésticos e caixas de visita, da estrutura de betão armado, incluindo arrumação de terras em depósito para aterros, compactação e				

(continues)

ATELIER DENSIDADES E UMA MARCA REGISTADA DA MUTABILIS9 ARTE E ARQUITECTURA,LDA.

DENSIDADES
ATELIER

ATELIER DENSIDADES
GABINETE DE ARQUITECTURA,
ENGENHARIA E TÉCNICAS AFINS,
IMAGENS 3D, DESIGN E DESIGN DE MOBILIÁRIO

CENTRO EMPRESARIAL
E INDUSTRIAL DE LOULÉ
CAMPINA DE BAIXO, LOTE 1 - SALA 4
8100-285 LOULÉ

t 00351 289 432 670
f 00351 289 432 671

info@densidades.pt
www.densidades.pt

Loulé, 30 May 2015

5 Clarification of detail regarding overflow of interior and exterior swimming pools and jacuzzi. - Solved. Details were send on the 30th of May in AutoCAD format. PDF prints of these will be updated in Andrew's online platform a.s.a.p.

6 Final versions of Kitchen, Pantry, Lounge, Playroom and Basement bar were updated and send to Lux in AutoCAD format. PDF prints of these will be updated in Andrew's online platform a.s.a.p.

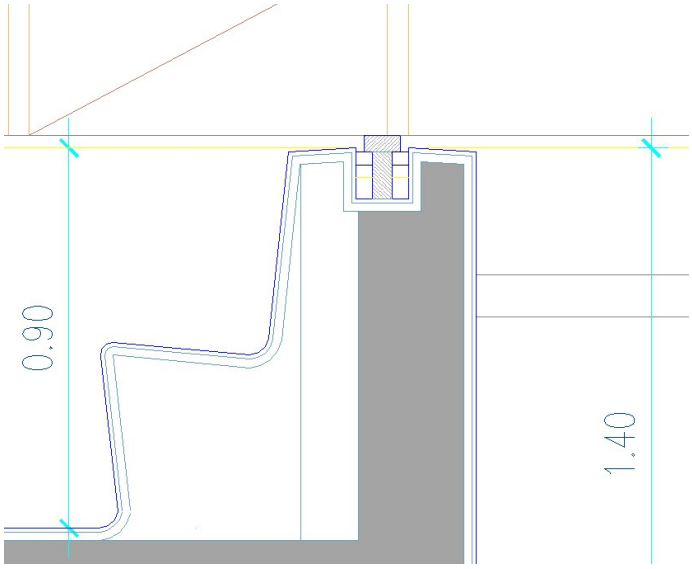

ATELIER DENSIDADES É UMA MARCA REGISTADA DA MUTABILIS9 ARTE E ARQUITECTURA,LDA.

DENSIDADES
ATELIER
